



# THE WHEEL

my TAKE → ASIS → TOBE • the first 90 days

Jim Clements Edition 1 • October 2026

# HALBERD

A 12-week SysML v1 to v2 port,  
run on the agile kit

---

Backlog, daily stand-ups, sprint burn-downs,  
funding and earned value

Halberd is fictional and notional, and so is every number here. It is the kit's worked example: one solutions architect ports a legacy SysML v1 model to SysML v2 text under a DevSecOps pipeline, 5 October to 23 December 2026.

## Contents

---

|          |                                                          |          |
|----------|----------------------------------------------------------|----------|
| <b>1</b> | <b>The program</b>                                       | <b>2</b> |
| <b>2</b> | <b>Backlog</b>                                           | <b>2</b> |
| <b>3</b> | <b>Release burn-down</b>                                 | <b>3</b> |
| <b>4</b> | <b>Funding and earned value</b>                          | <b>3</b> |
| 4.1      | Earned value at 30 October 2026 . . . . .                | 4        |
| 4.2      | Earned value at 25 November 2026 . . . . .               | 5        |
| 4.3      | Earned value at 23 December 2026 . . . . .               | 5        |
| <b>5</b> | <b>Sprints and daily stand-ups</b>                       | <b>5</b> |
| 5.1      | Sprint 1: 5 October 2026 to 16 October 2026 . . . . .    | 6        |
| 5.2      | Sprint 2: 19 October 2026 to 30 October 2026 . . . . .   | 7        |
| 5.3      | Sprint 3: 2 November 2026 to 13 November 2026 . . . . .  | 9        |
| 5.4      | Sprint 4: 16 November 2026 to 25 November 2026 . . . . . | 11       |
| 5.5      | Sprint 5: 30 November 2026 to 11 December 2026 . . . . . | 13       |
| 5.6      | Sprint 6: 14 December 2026 to 23 December 2026 . . . . . | 15       |

# 1 The program

Halberd's legacy SysML v1 model holds 1,960 in-scope items across seven organizations, and 1,450 DOORS requirements. One solutions architect ports it to SysML v2 text, one segment at a time, starting Monday 5 October 2026: two-week sprints, a baseline tagged every four weeks, and a stand-up every working day. The status meeting hears the alphabet: the 26 metrics A–Z of docs/STATUS-METRICS.html. Thanksgiving and 24–25 December are holidays, so the port runs 56 working days.

Everything here is computed by the kit, not typed. The project is a real kit project, built by compiling one stand-up file per day through the kit's own ledger; rebuild it and this document with one command:

---

```
perl sim/halberd-gen.pl --pdf                # data/halberd, docs/HALBERD.html and .pdf
perl bin/ledger.pl -f data/halberd/scrumbal Sprint:3 # the ledger: 330 items done in sprint 3
perl agile.pl --today 2026-11-05 data/halberd    # the cockpit on a blocked day
```

---

# 2 Backlog

The tome is *Halberd SysML v2 port*; its epics are the seven segments, in the order they are ported. Each task ports one day's worth of v1 items, counted in items (the journal's unit). A carried task counts in the segment being worked when it was committed; the rows add up to all 1,960 items.

| Epic         | Segment                           | v1 items     | Tasks     | Worked        |
|--------------|-----------------------------------|--------------|-----------|---------------|
| E            | Systems Engineering & Integration | 368          | 12        | 10-05 – 10-20 |
| V            | Interceptor Development           | 350          | 11        | 10-21 – 11-03 |
| B            | Battle Management & Fire Control  | 330          | 10        | 11-04 – 11-17 |
| T            | Test & Evaluation                 | 292          | 7         | 11-18 – 11-25 |
| G            | Government Program Office         | 160          | 5         | 11-30 – 12-04 |
| M            | Manufacturing & Production        | 244          | 8         | 12-07 – 12-15 |
| L            | Logistics & Sustainment           | 216          | 6         | 12-16 – 12-23 |
| <b>Total</b> |                                   | <b>1,960</b> | <b>59</b> |               |

**Table 1:** Segments as epics.

### 3 Release burn-down

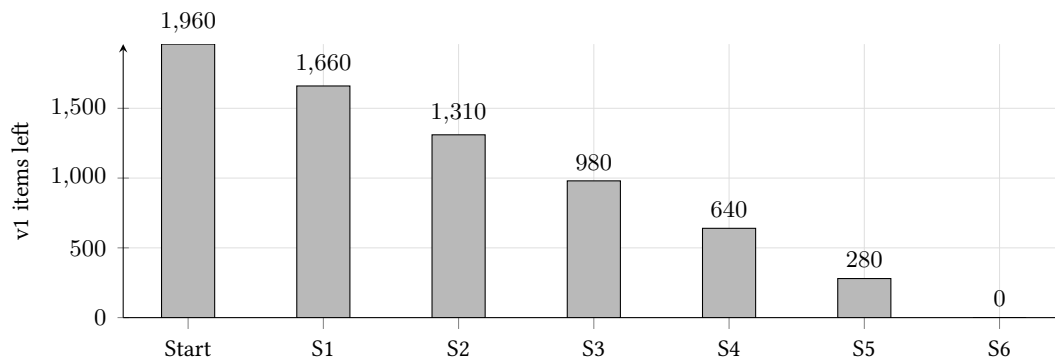


Figure 1: The whole v1 list, sprint by sprint.

| Sprint | Dates         | Committed | Done | Carried | Done % (X) | Items left |
|--------|---------------|-----------|------|---------|------------|------------|
| 1      | 10-05 – 10-16 | 320       | 300  | 20      | 94         | 1,660      |
| 2      | 10-19 – 10-30 | 360       | 350  | 10      | 97         | 1,310      |
| 3      | 11-02 – 11-13 | 375       | 330  | 45      | 88         | 980        |
| 4      | 11-16 – 11-25 | 360       | 340  | 20      | 94         | 640        |
| 5      | 11-30 – 12-11 | 370       | 360  | 10      | 97         | 280        |
| 6      | 12-14 – 12-23 | 280       | 280  | 0       | 100        | 0          |

Table 2: Sprint totals, computed from the compiled journal by `Scrum::sprint_summary`; the generator stops if any differs from the doc.

### 4 Funding and earned value

A notional FY27 funding journal sits beside the stand-up journal, in the same ledger format (data/halberd/funding.ledger). Each segment is budgeted at a notional \$150 per v1 item, time-phased over the days the plan works it. \$323,400 is authorized on 1 October: the budget at completion of \$294,000 plus a 10% reserve. Labor posts weekly from the items actually ported; sprint 3 overran while it waited on the shared runner. Percent complete comes from the stand-ups, so earned value is computed, not estimated.

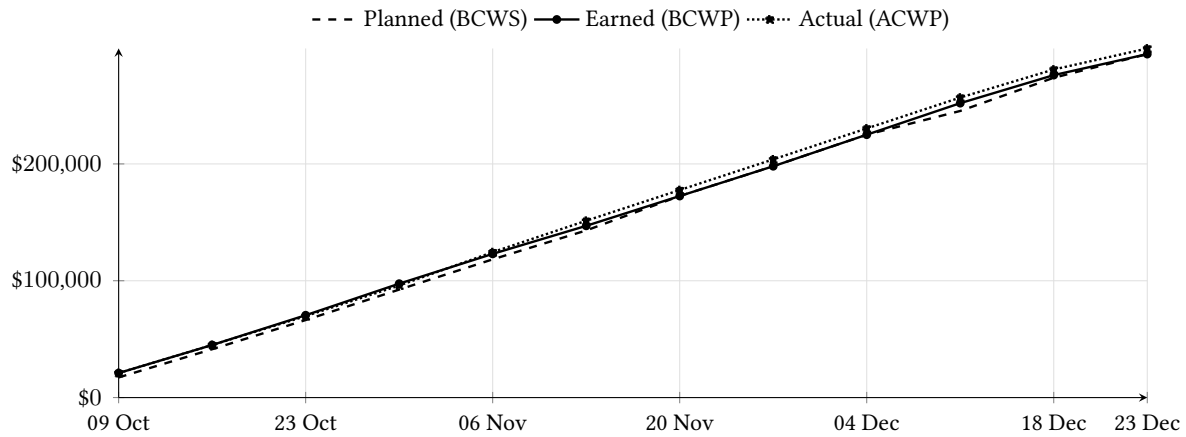


Figure 2: Cumulative cost at the end of each week.

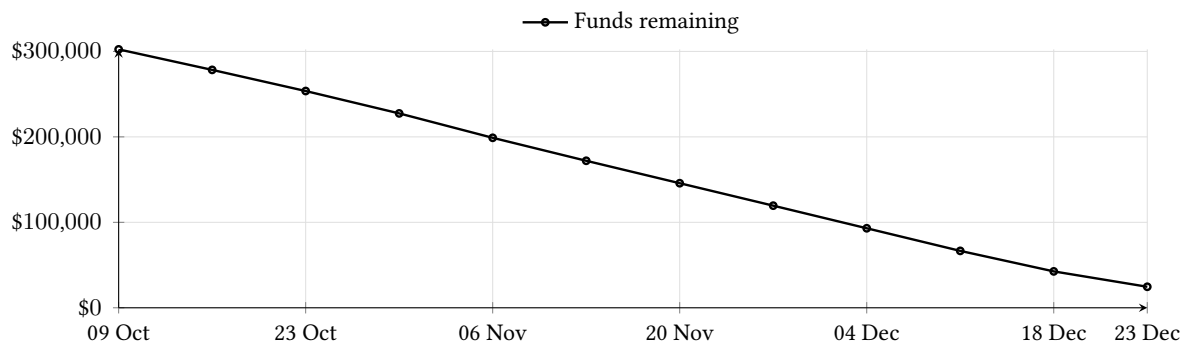


Figure 3: Funds remaining at the end of each week.

## 4.1 Earned value at 30 October 2026

| Segment                             | Done | BAC       | BCWS     | BCWP     | ACWP     | CV      | SV      | CPI  | SPI  | EAC       |
|-------------------------------------|------|-----------|----------|----------|----------|---------|---------|------|------|-----------|
| E Systems Engineering & Integration | 100% | \$55,200  | \$55,200 | \$55,200 | \$54,894 | \$306   | \$0     | 1.01 | 1.00 | \$54,894  |
| V Interceptor Development           | 81%  | \$52,500  | \$37,234 | \$42,300 | \$41,031 | \$1,269 | \$5,066 | 1.03 | 1.14 | \$50,925  |
| B Battle Management & Fire Control  | 0%   | \$49,500  | \$0      | \$0      | \$0      | \$0     | \$0     | –    | –    | –         |
| T Test & Evaluation                 | 0%   | \$40,800  | \$0      | \$0      | \$0      | \$0     | \$0     | –    | –    | –         |
| G Government Program Office         | 0%   | \$27,000  | \$0      | \$0      | \$0      | \$0     | \$0     | –    | –    | –         |
| M Manufacturing & Production        | 0%   | \$36,600  | \$0      | \$0      | \$0      | \$0     | \$0     | –    | –    | –         |
| L Logistics & Sustainment           | 0%   | \$32,400  | \$0      | \$0      | \$0      | \$0     | \$0     | –    | –    | –         |
| <b>Total</b>                        | 33%  | \$294,000 | \$92,434 | \$97,500 | \$95,925 | \$1,575 | \$5,066 | 1.02 | 1.05 | \$289,251 |

## 4.2 Earned value at 25 November 2026

| Segment                             | Done | BAC       | BCWS      | BCWP      | ACWP      | CV       | SV  | CPI  | SPI  | EAC       |
|-------------------------------------|------|-----------|-----------|-----------|-----------|----------|-----|------|------|-----------|
| E Systems Engineering & Integration | 100% | \$55,200  | \$55,200  | \$55,200  | \$54,894  | \$306    | \$0 | 1.01 | 1.00 | \$54,894  |
| V Interceptor Development           | 100% | \$52,500  | \$52,500  | \$52,500  | \$52,455  | \$45     | \$0 | 1.00 | 1.00 | \$52,455  |
| B Battle Management & Fire Control  | 100% | \$49,500  | \$49,500  | \$49,500  | \$54,522  | -\$5,022 | \$0 | 0.91 | 1.00 | \$54,522  |
| T Test & Evaluation                 | 100% | \$40,800  | \$40,800  | \$40,800  | \$42,024  | -\$1,224 | \$0 | 0.97 | 1.00 | \$42,024  |
| G Government Program Office         | 0%   | \$27,000  | \$0       | \$0       | \$0       | \$0      | \$0 | –    | –    | –         |
| M Manufacturing & Production        | 0%   | \$36,600  | \$0       | \$0       | \$0       | \$0      | \$0 | –    | –    | –         |
| L Logistics & Sustainment           | 0%   | \$32,400  | \$0       | \$0       | \$0       | \$0      | \$0 | –    | –    | –         |
| <b>Total</b>                        | 67%  | \$294,000 | \$198,000 | \$198,000 | \$203,895 | -\$5,895 | \$0 | 0.97 | 1.00 | \$302,753 |

Funds remaining \$119,505; average burn over the last two months \$95,925 a month; at that rate the money lasts 1.2 more months (to 2027-01-03).

## 4.3 Earned value at 23 December 2026

| Segment                             | Done | BAC       | BCWS      | BCWP      | ACWP      | CV       | SV  | CPI  | SPI  | EAC       |
|-------------------------------------|------|-----------|-----------|-----------|-----------|----------|-----|------|------|-----------|
| E Systems Engineering & Integration | 100% | \$55,200  | \$55,200  | \$55,200  | \$54,894  | \$306    | \$0 | 1.01 | 1.00 | \$54,894  |
| V Interceptor Development           | 100% | \$52,500  | \$52,500  | \$52,500  | \$52,455  | \$45     | \$0 | 1.00 | 1.00 | \$52,455  |
| B Battle Management & Fire Control  | 100% | \$49,500  | \$49,500  | \$49,500  | \$54,522  | -\$5,022 | \$0 | 0.91 | 1.00 | \$54,522  |
| T Test & Evaluation                 | 100% | \$40,800  | \$40,800  | \$40,800  | \$42,024  | -\$1,224 | \$0 | 0.97 | 1.00 | \$42,024  |
| G Government Program Office         | 100% | \$27,000  | \$27,000  | \$27,000  | \$26,460  | \$540    | \$0 | 1.02 | 1.00 | \$26,460  |
| M Manufacturing & Production        | 100% | \$36,600  | \$36,600  | \$36,600  | \$36,060  | \$540    | \$0 | 1.01 | 1.00 | \$36,060  |
| L Logistics & Sustainment           | 100% | \$32,400  | \$32,400  | \$32,400  | \$32,400  | \$0      | \$0 | 1.00 | 1.00 | \$32,400  |
| <b>Total</b>                        | 100% | \$294,000 | \$294,000 | \$294,000 | \$298,815 | -\$4,815 | \$0 | 0.98 | 1.00 | \$298,815 |

**At the finish:** \$298,815 spent against a \$294,000 budget (CPI 0.98); \$24,585 of the \$323,400 authorized is left, so the overrun came out of the reserve.


*CPI = earned / actual (above 1 is under cost); SPI = earned / planned (above 1 is ahead); EAC = BAC / CPI. The same numbers come from bin/ledger.pl evm and forecast.*

## 5 Sprints and daily stand-ups

Each stand-up answers yesterday, today and blockers, in the alphabet of the A–Z metrics. A dagger<sup>†</sup> marks a blocked day.

## 5.1 Sprint 1: 5 October 2026 to 16 October 2026

Committed 320. Done 300. Carried over 20. Done 94% (X).

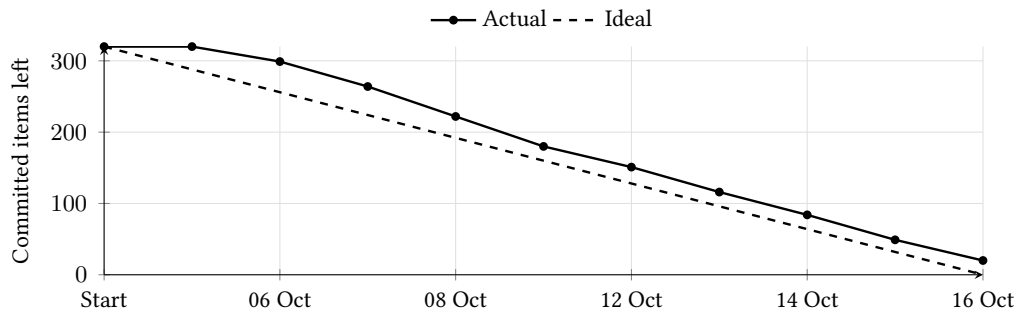


| Day        | Ported | Left  | Yesterday                                                                                                                                                                                                                                | Today                                                                             | Blockers |
|------------|--------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|----------|
| Mon 05 Oct | 0      | 1,960 | Nothing yet; the pipeline goes up today.                                                                                                                                                                                                 | Setting up the repo, the pre-commit gate and the CI lint job.                     | –        |
| Tue 06 Oct | 21     | 1,939 | The pipeline is up: pre-commit gate and CI lint job, 0/0 to merge (E).                                                                                                                                                                   | Continuing Systems Engineering & Integration.                                     | –        |
| Wed 07 Oct | 35     | 1,904 | 21 more elements under configuration control, now 1% (A), all merged at 0/0 (E).                                                                                                                                                         | More of Systems Engineering & Integration goes under configuration control today. | –        |
| Thu 08 Oct | 42     | 1,862 | 35 more elements under configuration control, now 3% (A), all merged at 0/0 (E).                                                                                                                                                         | Bringing more of Systems Engineering & Integration under the pipeline.            | –        |
| Fri 09 Oct | 42     | 1,820 | 42 more elements under configuration control, now 5% (A), all merged at 0/0 (E).                                                                                                                                                         | Continuing Systems Engineering & Integration.                                     | –        |
| Mon 12 Oct | 29     | 1,791 | 42 more elements under configuration control, now 7% (A), all merged at 0/0 (E).                                                                                                                                                         | Importing the first DOORS module.                                                 | –        |
| Tue 13 Oct | 35     | 1,756 | 29 more elements under configuration control, now 9% (A), all merged at 0/0 (E). The first DOORS module is in, and requirements are now linking to model elements (C). 2 orphan and 4 unverified requirements, flagged to owners (F, G). | Bringing more of Systems Engineering & Integration under the pipeline.            | –        |
| Wed 14 Oct | 32     | 1,724 | 35 more elements under configuration control, now 10% (A), all merged at 0/0 (E). 1 of 2 zone-crossing interfaces still need a security requirement (Q).                                                                                 | Continuing Systems Engineering & Integration.                                     | –        |
| Thu 15 Oct | 35     | 1,689 | 32 more elements under configuration control, now 12% (A), all merged at 0/0 (E). 54 of 1,450 DOORS requirements linked (C).                                                                                                             | More of Systems Engineering & Integration goes under configuration control today. | –        |
| Fri 16 Oct | 29     | 1,660 | 35 more elements under configuration control, now 14% (A), all merged at 0/0 (E). 3 interface mismatches caught at merge to date, 0 reached integration (H).                                                                             | Bringing more of Systems Engineering & Integration under the pipeline.            | –        |

*Notional: every name and number is made up.*

## 5.2 Sprint 2: 19 October 2026 to 30 October 2026

Committed 360. Done 350. Carried over 10. Done 97% (X). Includes HAL-10, 20 items carried in from sprint 1.

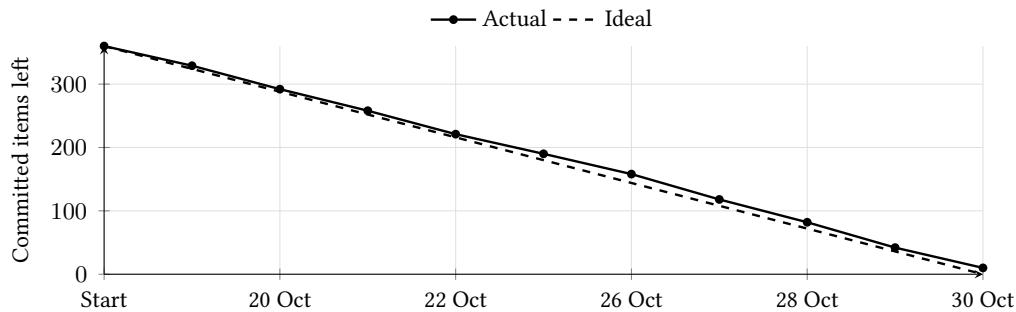


| Day        | Ported | Left  | Yesterday                                                                                                                                                                                                         | Today                                                                          | Blockers |
|------------|--------|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------|----------|
| Mon 19 Oct | 31     | 1,629 | 29 more elements under configuration control, now 15% (A), all merged at 0/0 (E). 12 orphan and 20 unverified requirements, flagged to owners (F, G).                                                             | Continuing Systems Engineering & Integration.                                  | –        |
| Tue 20 Oct | 37     | 1,592 | 31 more elements under configuration control, now 17% (A), all merged at 0/0 (E). 2 of 5 zone-crossing interfaces still need a security requirement (Q).                                                          | Finishing Systems Engineering & Integration; it should be gated by end of day. | –        |
| Wed 21 Oct | 34     | 1,558 | 37 more elements under configuration control, now 19% (A), all merged at 0/0 (E). Systems Engineering & Integration is now gated on every merge: 1 of 7 segments (B). 138 of 1,450 DOORS requirements linked (C). | Bringing more of Interceptor Development under the pipeline.                   | –        |
| Thu 22 Oct | 37     | 1,521 | 34 more elements under configuration control, now 21% (A), all merged at 0/0 (E). 8 interface mismatches caught at merge to date, 0 reached integration (H).                                                      | Continuing Interceptor Development.                                            | –        |
| Fri 23 Oct | 31     | 1,490 | 37 more elements under configuration control, now 22% (A), all merged at 0/0 (E). 36 orphan and 49 unverified requirements, flagged to owners (F, G).                                                             | More of Interceptor Development goes under configuration control today.        | –        |
| Mon 26 Oct | 32     | 1,458 | 31 more elements under configuration control, now 24% (A), all merged at 0/0 (E). 3 of 7 zone-crossing interfaces still need a security requirement (Q).                                                          | Bringing more of Interceptor Development under the pipeline.                   | –        |
| Tue 27 Oct | 40     | 1,418 | 32 more elements under configuration control, now 26% (A), all merged at 0/0 (E). 233 of 1,450 DOORS requirements linked (C).                                                                                     | Continuing Interceptor Development.                                            | –        |
| Wed 28 Oct | 36     | 1,382 | 40 more elements under configuration control, now 28% (A), all merged at 0/0 (E). 13 interface mismatches caught at merge to date, 0 reached integration (H).                                                     | More of Interceptor Development goes under configuration control today.        | –        |

| Day           | Ported | Left  | Yesterday                                                                                                                                                                                                                                                      | Today                                          | Blockers |
|---------------|--------|-------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------|----------|
| Thu 29<br>Oct | 40     | 1,342 | 36 more elements under configuration control, now 29% (A), all merged at 0/0 (E). 56 orphan and 70 unverified requirements, flagged to owners (F, G).                                                                                                          | Generating the interface table from the model. | –        |
| Fri 30<br>Oct | 32     | 1,310 | 40 more elements under configuration control, now 32% (A), all merged at 0/0 (E). The interface table is now generated from the model: 1 of 12 program documents (L), 0 hand edits (M). 2 of 9 zone-crossing interfaces still need a security requirement (Q). | Tagging baseline 1.                            | –        |

### 5.3 Sprint 3: 2 November 2026 to 13 November 2026

Committed 375. Done 330. Carried over 45. Done 88% (X). Includes HAL-21, 10 items carried in from sprint 2.

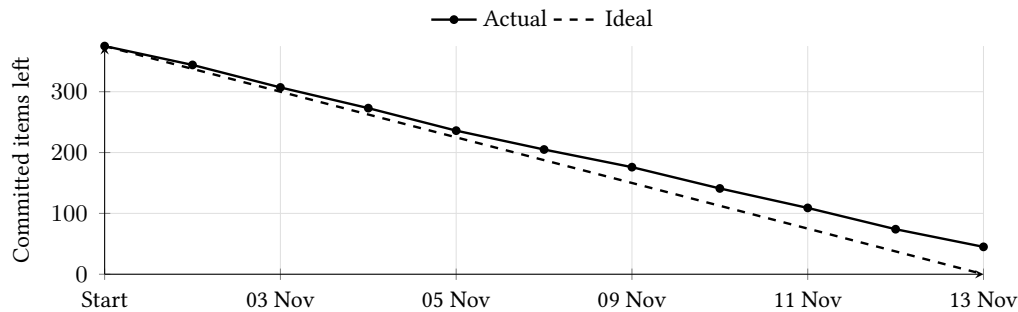


| Day                     | Ported | Left  | Yesterday                                                                                                                                                                                                                       | Today                                                                            | Blockers                                                                           |
|-------------------------|--------|-------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------|------------------------------------------------------------------------------------|
| Mon 02 Nov              | 31     | 1,279 | 32 more elements under configuration control, now 33% (A), all merged at 0/0 (E). Baseline 1 is tagged: 650 elements (D), and it rebuilds identically (S). 340 of 1,450 DOORS requirements linked (C).                          | More of Interceptor Development goes under configuration control today.          | –                                                                                  |
| Tue 03 Nov              | 37     | 1,242 | 31 more elements under configuration control, now 35% (A), all merged at 0/0 (E). 18 interface mismatches caught at merge to date, 0 reached integration (H).                                                                   | Finishing Interceptor Development; it should be gated by end of day.             | –                                                                                  |
| Wed 04 Nov <sup>†</sup> | 34     | 1,208 | 37 more elements under configuration control, now 37% (A), all merged at 0/0 (E). Interceptor Development is now gated on every merge: 2 of 7 segments (B). 63 orphan and 78 unverified requirements, flagged to owners (F, G). | Continuing Battle Management & Fire Control.                                     | Waiting on a shared runner. Gating locally with the pre-commit hook meanwhile (Y). |
| Thu 05 Nov <sup>†</sup> | 37     | 1,171 | 34 more elements under configuration control, now 38% (A), all merged at 0/0 (E).                                                                                                                                               | More of Battle Management & Fire Control goes under configuration control today. | Still waiting on the shared runner (Y).                                            |
| Fri 06 Nov <sup>†</sup> | 31     | 1,140 | 37 more elements under configuration control, now 40% (A), all merged at 0/0 (E). 454 of 1,450 DOORS requirements linked (C).                                                                                                   | Bringing more of Battle Management & Fire Control under the pipeline.            | Runner still pending; asked for it again (Y).                                      |
| Mon 09 Nov              | 29     | 1,111 | 31 more elements under configuration control, now 42% (A), all merged at 0/0 (E). 25 interface mismatches caught at merge to date, 0 reached integration (H). The shared runner is live.                                        | Continuing Battle Management & Fire Control.                                     | –                                                                                  |
| Tue 10 Nov              | 35     | 1,076 | 29 more elements under configuration control, now 43% (A), all merged at 0/0 (E). 56 orphan and 72 unverified requirements, flagged to owners (F, G).                                                                           | More of Battle Management & Fire Control goes under configuration control today. | –                                                                                  |
| Wed 11 Nov              | 32     | 1,044 | 35 more elements under configuration control, now 45% (A), all merged at 0/0 (E). 3 of 14 zone-crossing interfaces still need a security requirement (Q).                                                                       | Generating the first ICD view and diffing it against the legacy ICD.             | –                                                                                  |

*Notional: every name and number is made up.*

| Day           | Ported | Left  | Yesterday                                                                                                                                                                                                         | Today                                                                            | Blockers |
|---------------|--------|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------|----------|
| Thu 12<br>Nov | 35     | 1,009 | 32 more elements under configuration control, now 47% (A), all merged at 0/0 (E). Drift checks found 47 discrepancies in the legacy ICDs, flagged for correction (T). 558 of 1,450 DOORS requirements linked (C). | Continuing Battle Management & Fire Control.                                     | –        |
| Fri 13<br>Nov | 29     | 980   | 35 more elements under configuration control, now 49% (A), all merged at 0/0 (E). 30 interface mismatches caught at merge to date, 0 reached integration (H).                                                     | More of Battle Management & Fire Control goes under configuration control today. | –        |

## 5.4 Sprint 4: 16 November 2026 to 25 November 2026

Committed 360. Done 340. Carried over 20. Done 94% (X). Includes HAL-32, 45 items carried in from sprint 3.

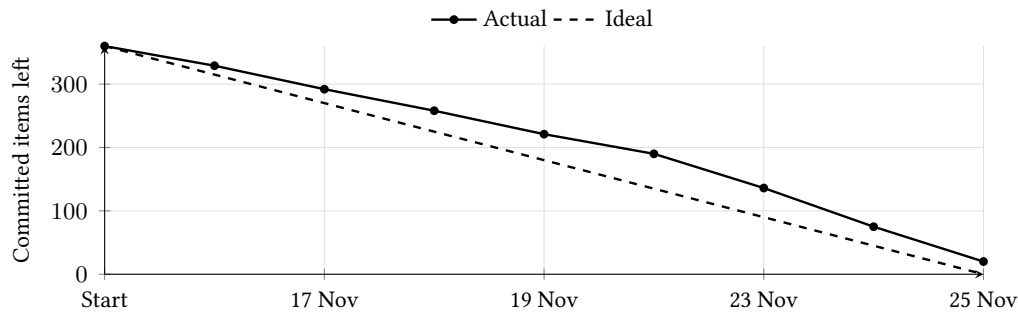


| Day        | Ported | Left | Yesterday                                                                                                                                                                                                                                                               | Today                                                                         | Blockers |
|------------|--------|------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------|----------|
| Mon 16 Nov | 31     | 949  | 29 more elements under configuration control, now 50% (A), all merged at 0/0 (E). 47 orphan and 63 unverified requirements, flagged to owners (F, G).                                                                                                                   | Bringing more of Battle Management & Fire Control under the pipeline.         | –        |
| Tue 17 Nov | 37     | 912  | 31 more elements under configuration control, now 52% (A), all merged at 0/0 (E). 1 of 16 zone-crossing interfaces still need a security requirement (Q).                                                                                                               | Finishing Battle Management & Fire Control; it should be gated by end of day. | –        |
| Wed 18 Nov | 34     | 878  | 37 more elements under configuration control, now 53% (A), all merged at 0/0 (E). Battle Management & Fire Control is now gated on every merge: 3 of 7 segments (B). 3 of 7 segment owners now merge their own changes (Z). 670 of 1,450 DOORS requirements linked (C). | More of Test & Evaluation goes under configuration control today.             | –        |
| Thu 19 Nov | 37     | 841  | 34 more elements under configuration control, now 55% (A), all merged at 0/0 (E). 36 interface mismatches caught at merge to date, 0 reached integration (H).                                                                                                           | Bringing more of Test & Evaluation under the pipeline.                        | –        |
| Fri 20 Nov | 31     | 810  | 37 more elements under configuration control, now 57% (A), all merged at 0/0 (E). 51 orphan and 61 unverified requirements, flagged to owners (F, G).                                                                                                                   | Continuing Test & Evaluation.                                                 | –        |
| Mon 23 Nov | 54     | 756  | 31 more elements under configuration control, now 59% (A), all merged at 0/0 (E). 3 of 19 zone-crossing interfaces still need a security requirement (Q).                                                                                                               | More of Test & Evaluation goes under configuration control today.             | –        |
| Tue 24 Nov | 61     | 695  | 54 more elements under configuration control, now 61% (A), all merged at 0/0 (E). 804 of 1,450 DOORS requirements linked (C).                                                                                                                                           | Wiring the T2 pre-flight prediction inputs to the model.                      | –        |

| Day           | Ported | Left | Yesterday                                                                                                                                                                                                                                                                                  | Today                                  | Blockers |
|---------------|--------|------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------|----------|
| Wed 25<br>Nov | 55     | 640  | 61 more elements under configuration control, now 65% (A), all merged at 0/0 (E). 64 of 64 pre-flight prediction parameters now come from the model (O), and 12 of 12 prediction runs name their baseline (P). 41 interface mismatches caught at merge to date, 0 reached integration (H). | Tagging baseline 2 before the holiday. | –        |

## 5.5 Sprint 5: 30 November 2026 to 11 December 2026

Committed 370. Done 360. Carried over 10. Done 97% (X). Includes HAL-40, 20 items carried in from sprint 4.

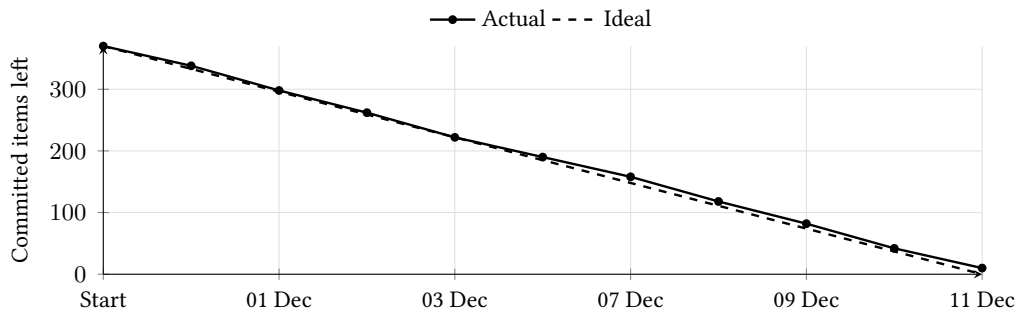

| Day        | Ported | Left | Yesterday                                                                                                                                                                                                                                                                                                                                            | Today                                                                      | Blockers |
|------------|--------|------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------|----------|
| Mon 30 Nov | 32     | 608  | 55 more elements under configuration control, now 67% (A), all merged at 0/0 (E). Test & Evaluation is now gated on every merge: 4 of 7 segments (B). 4 of 7 segment owners now merge their own changes (Z). Baseline 2 is tagged: 1,320 elements (D), rebuilds identically (S). 39 orphan and 48 unverified requirements, flagged to owners (F, G). | More of Government Program Office goes under configuration control today.  | –        |
| Tue 01 Dec | 40     | 568  | 32 more elements under configuration control, now 69% (A), all merged at 0/0 (E).                                                                                                                                                                                                                                                                    | Bringing more of Government Program Office under the pipeline.             | –        |
| Wed 02 Dec | 36     | 532  | 40 more elements under configuration control, now 71% (A), all merged at 0/0 (E). 960 of 1,450 DOORS requirements linked (C).                                                                                                                                                                                                                        | Continuing Government Program Office.                                      | –        |
| Thu 03 Dec | 40     | 492  | 36 more elements under configuration control, now 73% (A), all merged at 0/0 (E).                                                                                                                                                                                                                                                                    | Reviewing threat and mitigation coverage with the ISSM.                    | –        |
| Fri 04 Dec | 32     | 460  | 40 more elements under configuration control, now 75% (A), all merged at 0/0 (E). 2 of 12 recorded threats lack a traced mitigation (R). 30 orphan and 37 unverified requirements, flagged to owners (F, G).                                                                                                                                         | Measuring lead time on the last 10 merges.                                 | –        |
| Mon 07 Dec | 32     | 428  | 32 more elements under configuration control, now 77% (A), all merged at 0/0 (E). Government Program Office is now gated on every merge: 5 of 7 segments (B). 5 of 7 segment owners now merge their own changes (Z). A model change now reaches a reviewed baseline in 4 days; the old change board cycle took 19 (N).                               | Continuing Manufacturing & Production.                                     | –        |
| Tue 08 Dec | 40     | 388  | 32 more elements under configuration control, now 78% (A), all merged at 0/0 (E). 1,078 of 1,450 DOORS requirements linked (C).                                                                                                                                                                                                                      | More of Manufacturing & Production goes under configuration control today. | –        |


*Notional: every name and number is made up.*

| Day           | Ported | Left | Yesterday                                                                                                                                                                                                                                                          | Today                                                                      | Blockers |
|---------------|--------|------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------|----------|
| Wed 09<br>Dec | 36     | 352  | 40 more elements under configuration control, now 80% (A), all merged at 0/0 (E). 47 interface mismatches caught at merge to date, 0 reached integration (H).                                                                                                      | Generating the remaining ICD views.                                        | –        |
| Thu 10<br>Dec | 40     | 312  | 36 more elements under configuration control, now 82% (A), all merged at 0/0 (E). 8 of 12 program documents now come straight from the model (L), about 30 labor hours saved per baseline (J). 21 orphan and 27 unverified requirements, flagged to owners (F, G). | Continuing Manufacturing & Production.                                     | –        |
| Fri 11<br>Dec | 32     | 280  | 40 more elements under configuration control, now 84% (A), all merged at 0/0 (E). 0 of 25 zone-crossing interfaces still need a security requirement (Q).                                                                                                          | More of Manufacturing & Production goes under configuration control today. | –        |

*Notional: every name and number is made up.*

## 5.6 Sprint 6: 14 December 2026 to 23 December 2026

Committed 280. Done 280. Carried over 0. Done 100% (X). Includes HAL-51, 10 items carried in from sprint 5.

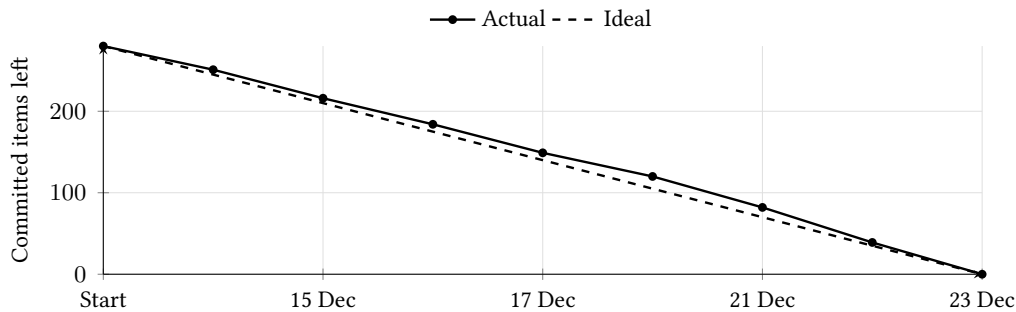

| Day        | Ported | Left | Yesterday                                                                                                                                                                                                                                                                                 | Today                                                                   | Blockers |
|------------|--------|------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------|----------|
| Mon 14 Dec | 29     | 251  | 32 more elements under configuration control, now 86% (A), all merged at 0/0 (E). 1,210 of 1,450 DOORS requirements linked (C).                                                                                                                                                           | Bringing more of Manufacturing & Production under the pipeline.         | –        |
| Tue 15 Dec | 35     | 216  | 29 more elements under configuration control, now 87% (A), all merged at 0/0 (E).                                                                                                                                                                                                         | Finishing Manufacturing & Production; it should be gated by end of day. | –        |
| Wed 16 Dec | 32     | 184  | 35 more elements under configuration control, now 89% (A), all merged at 0/0 (E). Manufacturing & Production is now gated on every merge: 6 of 7 segments (B). 6 of 7 segment owners now merge their own changes (Z). 13 orphan and 18 unverified requirements, flagged to owners (F, G). | Rebuilding the gate after this morning's parser update.                 | –        |
| Thu 17 Dec | 35     | 149  | 32 more elements under configuration control, now 91% (A), all merged at 0/0 (E). The gate broke on a parser update and was restored in 2 hours (W). ICD views regenerate in 6 minutes (K).                                                                                               | Bringing more of Logistics & Sustainment under the pipeline.            | –        |
| Fri 18 Dec | 29     | 120  | 35 more elements under configuration control, now 92% (A), all merged at 0/0 (E). 1,333 of 1,450 DOORS requirements linked (C).                                                                                                                                                           | Continuing Logistics & Sustainment.                                     | –        |
| Mon 21 Dec | 38     | 82   | 29 more elements under configuration control, now 94% (A), all merged at 0/0 (E).                                                                                                                                                                                                         | More of Logistics & Sustainment goes under configuration control today. | –        |
| Tue 22 Dec | 43     | 39   | 38 more elements under configuration control, now 96% (A), all merged at 0/0 (E). 6 orphan and 9 unverified requirements, flagged to owners (F, G).                                                                                                                                       | Bringing more of Logistics & Sustainment under the pipeline.            | –        |
| Wed 23 Dec | 39     | 0    | 43 more elements under configuration control, now 98% (A), all merged at 0/0 (E).                                                                                                                                                                                                         | Tagging baseline 3.                                                     | –        |

*Notional: every name and number is made up.*
